


IMPLEMENTATION PROGRAMME

MIAMI/SANTIAGO AND SAO PAULO-RIO DE JANEIRO/MIAMI RNAV ROUTES TRIAL

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18
ID	Task Name	Duration	Start	Finish	Predecessors	March	April	May	June	July	August	September	October	November	December	January	February
						Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
1	Prepare/Send State letter to affected States	18 days	Mon 3/27/00	Wed 4/14/00													
2	RNAV Seminar	5 days	Mon 3/27/00	Fri 3/31/00													
3	Draft routes Definition	3 days	Tue 3/28/00	Fri 3/31/00													
4	Sao Paulo-Miami	3 days	Tue 3/28/00	Fri 3/31/00													
5	Santiago-Miami	3 days	Tue 3/28/00	Fri 3/31/00													
6	State/Org Route Coordination	25 days	Mon 4/24/00	Fri 5/19/00	3.1												
7	Develop Briefing/Training Req.	15 days	Mon 5/1/00	Fri 5/19/00													
8	Flight Plan Filing Requirem.	10 days	Mon 5/1/00	Fri 5/12/00													
9	Develop ATC Procedures	15 days	Tue 5/2/00	Fri 5/19/00													
10	Define final routes and FIR crossing point	7 days	Mon 5/8/00	Fri 5/12/00	6												
11	Prepare Briefings States/Carrier	25 days	Mon 5/1/00	Fri 6/16/00	11												
12	Charting Requirements	15 days	Mon 5/1/00	Fri 6/2/00	11												
13	Chart Production	60 days	Mon 6/5/00	Fri 8/25/00	13												
14	ACC/Air Carrier Principals Meeting	4 days	Tue 7/18/00	Fri 7/21/00	7,8,9,10,11,12												
15	Program Flight Trials	60 days	Thu 7/20/00	Fri 9/15/00													
16	Pre-trials meetings	4 days	Mon 9/18/00	Thu 9/21/00	16												
17	Publication of route/	3 days	Fri 9/22/00	Tue 9/26/00	17												
18	Trial Flights	91 days	Mon 10/02/00	Fri 1/12/01	17.18												
19	Data Collection	91 days	Mon 10/02/00	Fri 1/12/01													
20	Data Processing	6 days	Fri 1/12/01	Fri 1/19/01	20												
21	Evaluation Feedback Meeting	3 days	Mon 1/22/01	We 1/24/01	21												

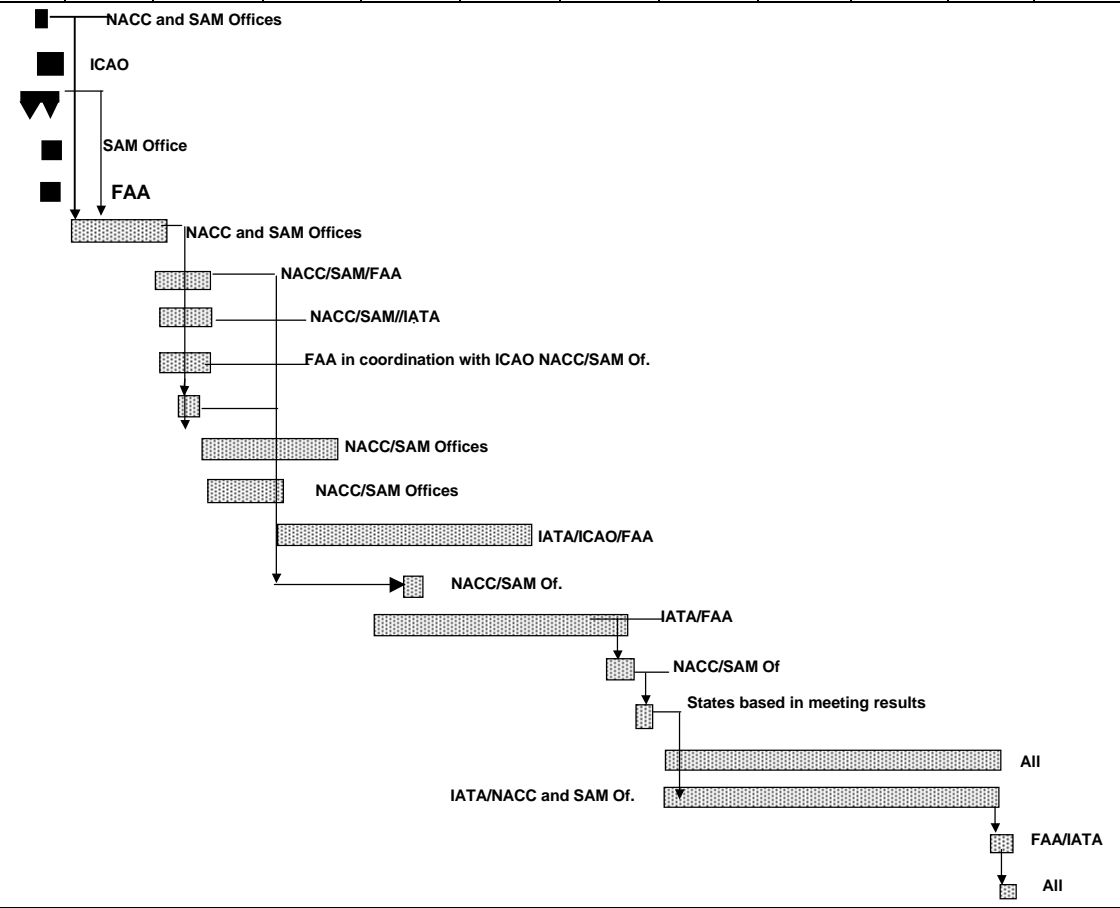

h:\meeting\implant. RNAV\wp5appa.xls

Date: 12.7.00

