WP02B: Follow-up on AASPG/1 Conclusions and Decisions

AASPG/2 Meeting, 2-6 Nov 2026

Livingstone, Zambia

INTERNATIONAL CIVIL AVIATION ORGANIZATION



ICAO Secretariat

Mrs. Chinga Mazhetese: Regional Officer: ENV/ MET (ESAF)

Overview

48%

of the 33 Conclusions and Decisions completed (16)

10 of 17


In Progress items are overdue at AASPG/2

- Overdue items are concentrated in:
  - IWXXM transition, SMO/SG operationalisation, Abuja Safety Targets monitoring, ARMA governance, AASPG reporting and ICAO guidance material.
- Recurring constraints:
  - delayed State reporting, limited availability of nominated experts, non-response from implementing organisations.


Status of implementation

Conclusions and Decisions of AASPG/1 (33), status as reported in the Appendix

All items

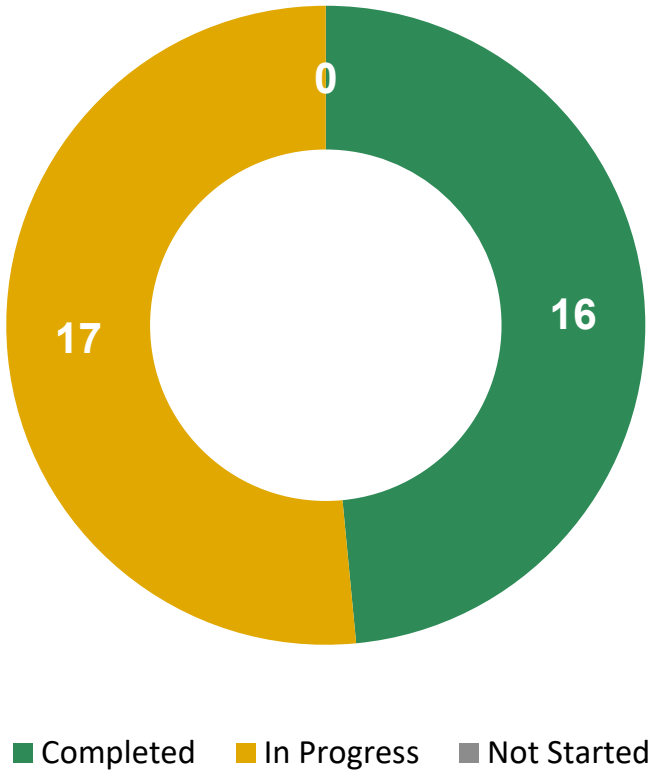

Breakdown of items not yet completed

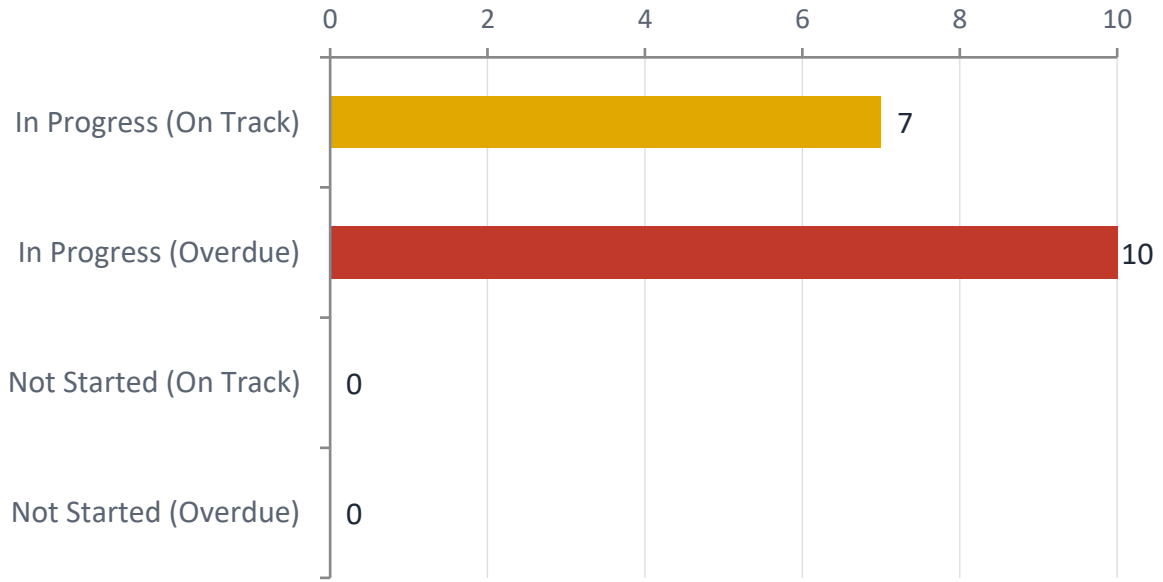

No items reported as Not Started. 17 items in progress


Status of deliverables by responsible party

Main deliverables derived from the 33 Conclusions and Decisions

Conc./Dec. No Strategic Objective	Title of Conc./Dec.	Text of Conclusion / Decisions	Responsibility	Deliverable	Report / Completion Date	Status of Implementation
1	2	3	4	5	6	7
			AASPG/1			
Conclusion 1/05	***AFI SAR Plan Update***	That to enhance and harmonize SAR implementation in the AFI region, a) The amended English version and the new French version of the AFI SAR Plan for the cycle 2025-2028 are endorsed. b) States are urged to update their national Plan to align with the AFI SAR plan.	**a) AASPG** **b) States**	**Number of States with updated national SAR Plan**	a) 7 November 2025 b) 30 October 2027	**In Progress (On Track)** a) Completed. The AFI SAR Plan was endorsed at the AASPG/1 Meeting. b) Status of the update of national SAR Plans to be notified by States. The comprehensive status of State national SAR plan will be updated after the cyclical survey of 2028.
Conclusion 1/06	***Establishment of the AFI 30/10 Project Management Team***	That to improve and optimize air traffic management in the AFI continental and Oceanic airspaces and to ensure the timely and effective implementation of reduced longitudinal separation, a) The AFI 30/10 project management team is established. The Terms of Reference and related project document are endorsed. b) Secretariat and States to coordinate the selection of qualified project team members.	**a) AASPG** **b) ICAO & States**	**AFI 30/10 PMT Members selected** **AFI 30/10 PMT established**	a) 7 November 2025 b) 31 March 2026	**Completed** a) Completed. b) Completed. The Project Team members were selected.
Decision 1/07	***Endorsement of the AFI A-CDM***	That to support the harmonized implementation of A-CDM in the Region,	**AASPG**	**Not applicable**	7 November 2025	**Completed** The AFI A-CDM implementation

Status of deliverables by responsible party

- *Most were with the Secretariat*

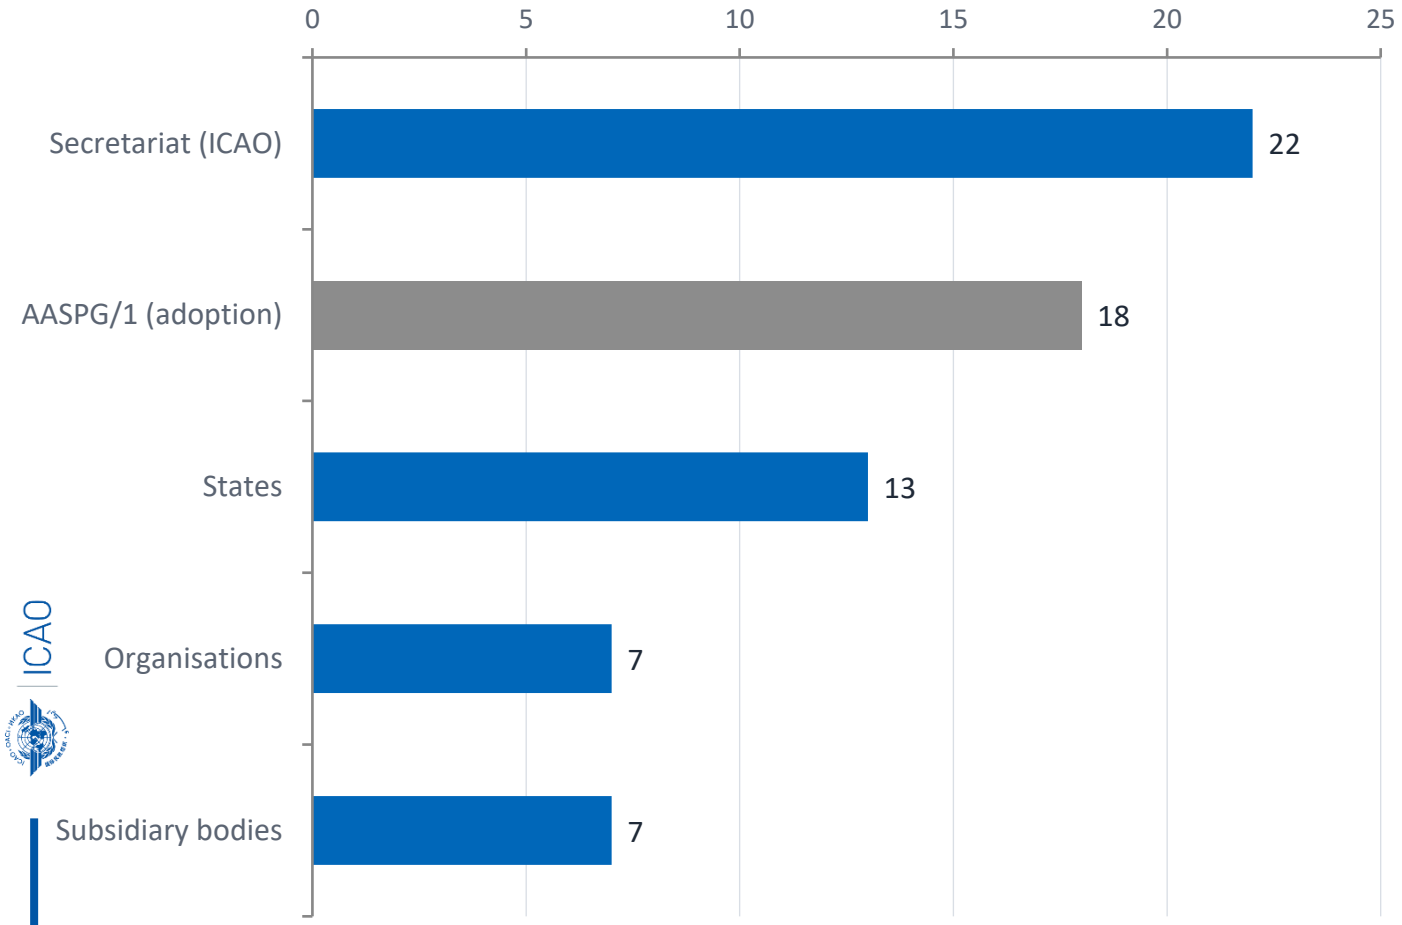


Overview

- Secretariat: 22 deliverables
  - coordination, workshops, guidance and reporting tools.
- States: 13 deliverables:
  - national plans, reporting, experts and IWXXM systems.
- Organisations (AFCAC, ASECNA, IATA, ARMA):
  - 7 deliverables, mostly technical and time-bound.
- AASPG/1 (grey):
  - 18 Decisions given effect on adoption.

Number and Status of deliverables by responsible party

While progress has been made, some Organizations and States continue to require additional support to advance implementation.

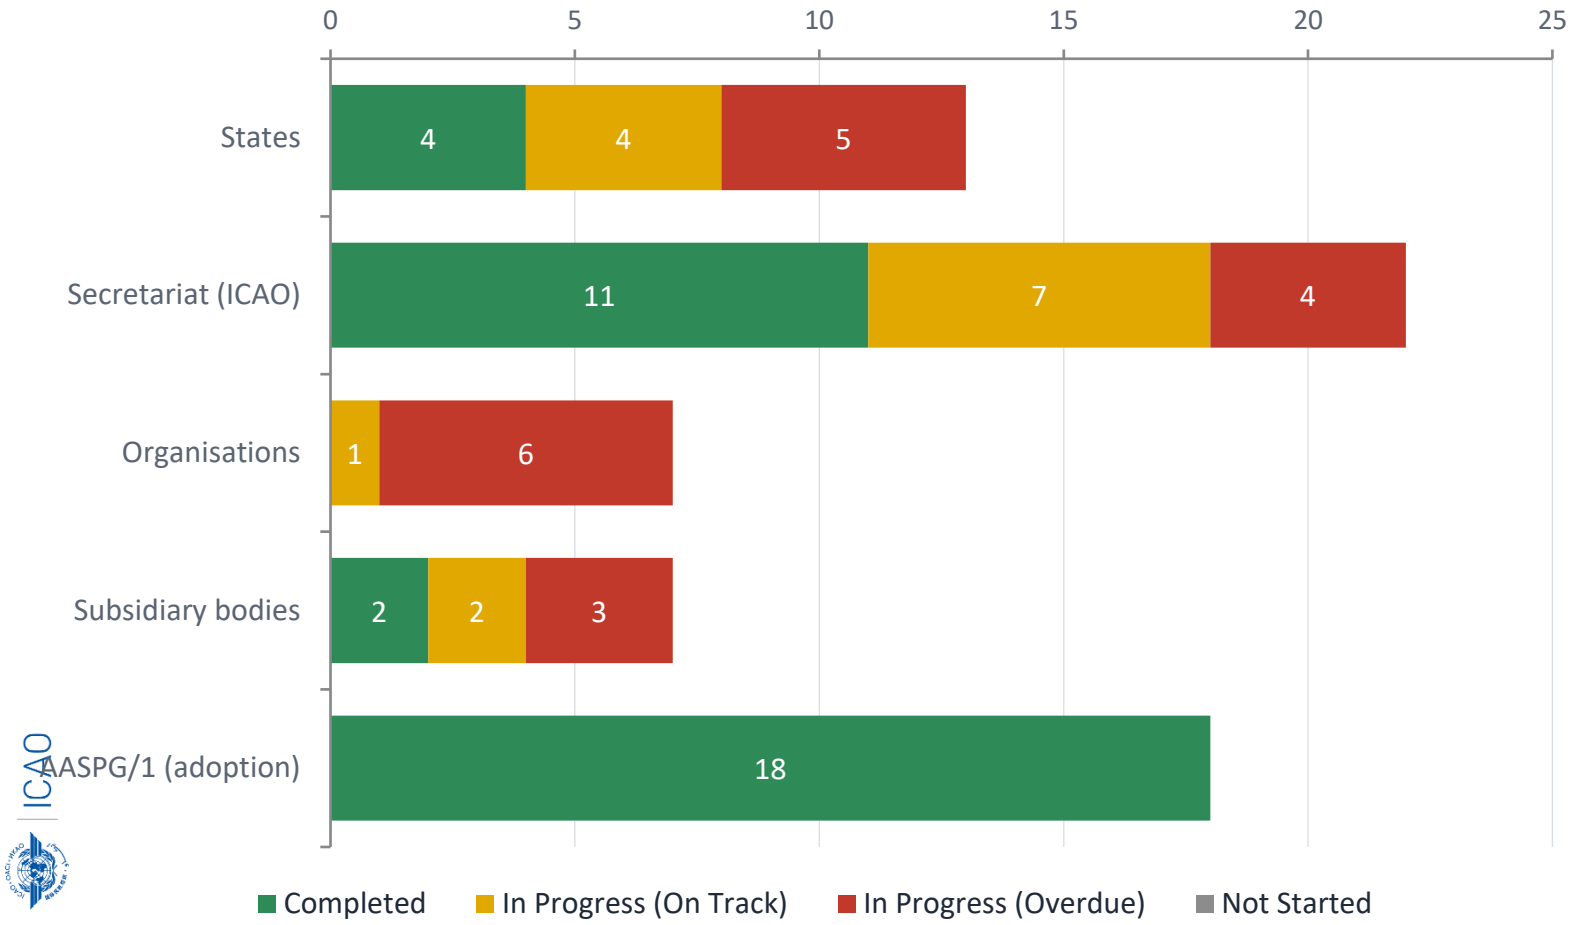

Completion rate

31%	States
50%	Secretariat (ICAO)
0%	Organisations
29%	Subsidiary bodies

Not Started: no deliverable reported in this category.

Upcoming and Outstanding Deliverables

On-track deliverables: but still to be delivered

Due	Deliverable	Responsible Party
AASPG/2	1/26 b) ANS Summit coordination and update	ICAO & IATA
AASPG/2	1/33 a)–b) RSP analysis; Additional OLS guidance material under development.	ICAO
30 Nov 2026	1/14 f) REDDIG feasibility; AMHS workshop	ASECNA
30 Nov 2026	1/19 & 1/28 SAT mandate and Handbook	SAT bodies
31 Dec 2026	1/10 BBB monitoring mechanism	Secretariat
31 Dec 2026	1/14 e) BCC IWXXM deployment	States (BCCs)
31 Dec 2026	1/17 Volcanic events workshop	Secretariat
2027	1/04 b)–c), 1/05 b) SAR documentation and plans	ICAO, States
No date	1/02 a) ASTs in national plans	States

Factors Affecting Implementation

States

- Delayed or incomplete reporting
- Limited participation, release and sponsorship of nominated AASPG SG experts
- Technical and infrastructure constraints in the AMHS FTBP and IWXXM transition

Items: 1/02, 1/08, 1/14, 1/23

Secretariat (ICAO)

- Dependence on third-party responses (States and/or Organisations)
- AART not yet established; WP to be presented on this matter.
- Reliance on ICAO HQ for global guidance (PBCS, Annex 14, conflict zones)

Items: 1/14 f), 1/32 b), 1/33

Organisations

- Non-response from Organisations e.g on IWXXM, AMHS FTBP, RODB VPN link and REDDIG node
- Framework for the Abuja Safety Targets
- ARMA governance study slowed by the data required from several institutions

Items: 1/02 b), 1/14 a)–c), 1/29 b)

Thank You



ICAO
